




Assembly Job Gantt Chart

11/29/06

Order: XB355

Job ID	Assy Job	Job Description	Qty	Rel Date Due Date	Days Early <Late>	Estimated Start Date	Estimated Finish Date
XB355A		30-150-WC-<200 Q>1	2.00	07/02-06:00a 07/14-11:59p	2.60	07/07-03:54p	07/12-10:21a
XB355G	XB355A	3-75-DV	2.00	07/02-06:00a 07/08-11:59p	2.40	07/06-07:00a	07/06-02:02p
XB355H	XB355A	ALL WELD W/MANHOLE	2.00	07/02-06:00a 07/06-11:59p	4.00	07/02-06:00a	07/03-12:20a
XB355K	XB355A	CAB PARTS-WC-SBLAST	2.00	07/02-06:00a 07/08-11:59p	2.90	07/05-08:48a	07/06-01:20a
XB355L	XB355A	30-225-WC-NR Q=1	2.00	07/02-06:00a 07/07-11:59p	2.70	07/02-06:00a	07/05-07:05a
XB355C	XB355G	75-3PH-3-COILS STD	2.00	07/02-06:00a 07/07-11:59p	4.80	07/02-06:00a	07/03-05:33a

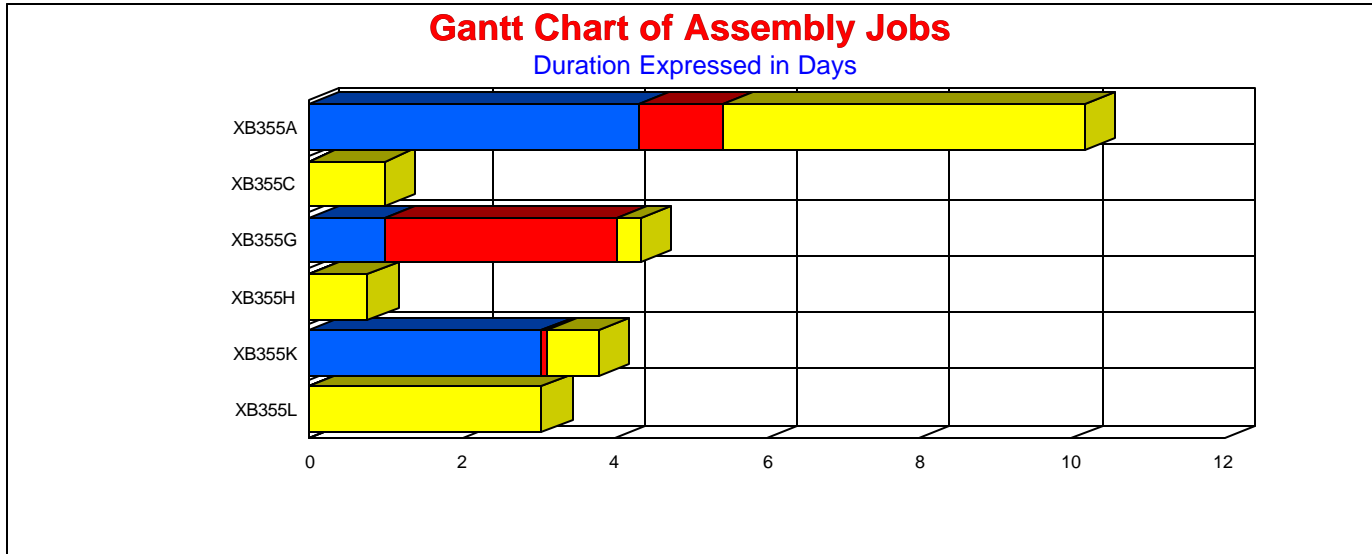




Assembly Job Gantt Chart

11/29/06

Order: XB356

Job ID	Assy Job	Job Description	Qty	Rel Date Due Date	Days Early <Late>	Estimated Start Date	Estimated Finish Date
XB356A		30-150-WC-<200 Q>1	3.00	07/02-06:00a 07/14-11:59p	1.60	07/07-05:18p	07/13-10:39a
XB356G	XB356A	3-150-DV	3.00	07/02-06:00a 07/06-11:59p	4.60	07/02-06:00a	07/02-10:45a
XB356H	XB356A	ALL WELD W/MANHOLE	3.00	07/02-06:00a 07/07-11:59p	2.40	07/02-06:24a	07/05-01:14p
XB356K	XB356A	CAB PARTS-WC-SBLAST	3.00	07/02-06:00a 07/08-11:59p	2.00	07/06-07:59a	07/06-11:56p
XB356L	XB356A	30-225-WC-NR Q=1	3.00	07/02-06:00a 07/08-11:59p	2.70	07/02-06:00a	07/06-07:59a

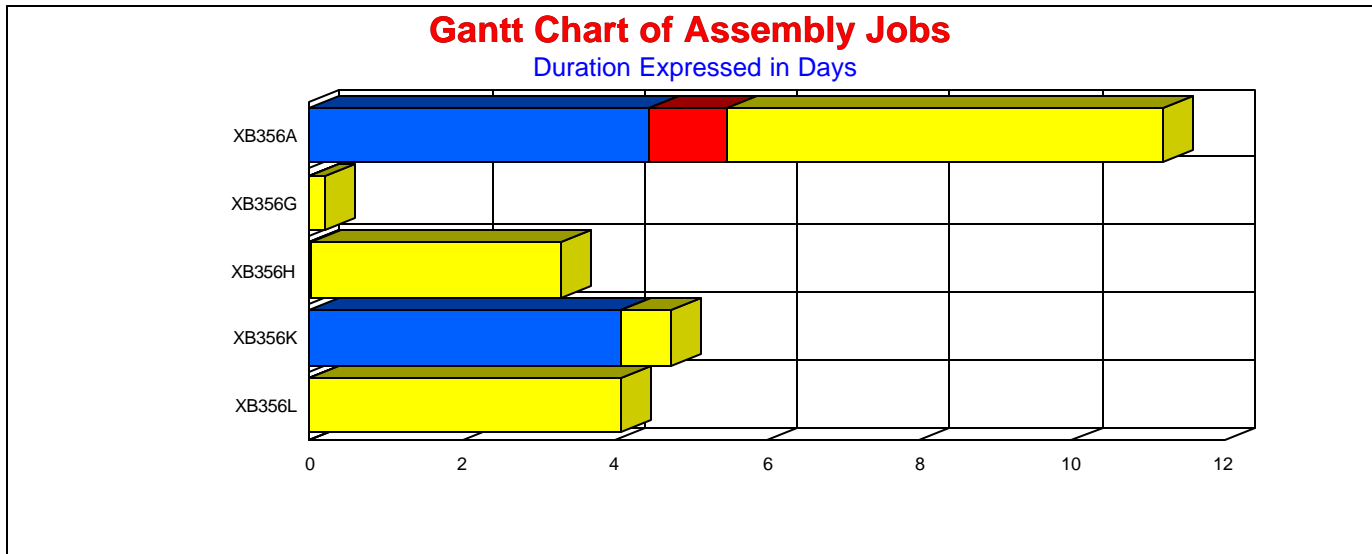




Assembly Job Gantt Chart

11/29/06

Order: XB357

Job ID	Assy Job	Job Description	Qty	Rel Date Due Date	Days Early <Late>	Estimated Start Date	Estimated Finish Date
XB357A		30-150-WC-<200 Q>1	3.00	07/02-06:00a 07/16-11:59p	2.40	07/09-02:34a	07/14-01:47p
XB357G	XB357A	3-150-DV	3.00	07/02-06:00a 07/06-11:59p	4.40	07/02-06:00a	07/02-01:15p
XB357H	XB357A	ALL WELD W/MANHOLE	3.00	07/02-06:00a 07/08-11:59p	2.30	07/02-08:48a	07/06-03:38p
XB357K	XB357A	CAB PARTS-WC-SBLAST	3.00	07/02-06:00a 07/13-11:59p	4.60	07/08-01:11p	07/09-09:44a
XB357L	XB357A	30-225-WC-NR Q=1	3.00	07/02-06:00a 07/10-11:59p	2.50	07/07-07:36a	07/08-01:11p
XB357J	XB357L	WELD ON FF QTY=1	3.00	07/02-06:00a 07/07-11:59p	2.50	07/02-07:00a	07/05-11:48a

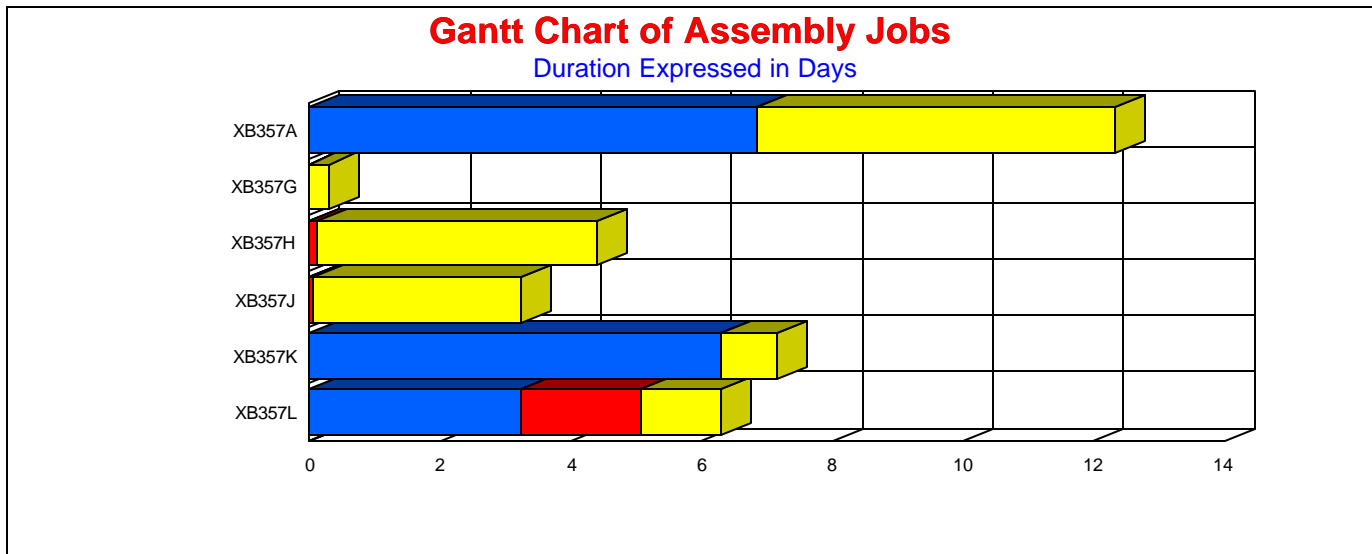




Assembly Job Gantt Chart

11/29/06

Order: XB358

Job ID	Assy Job	Job Description	Qty	Rel Date Due Date	Days Early <Late>	Estimated Start Date	Estimated Finish Date
XB358A		225-500-WC-<200 Q>1	4.00	07/02-06:00a 07/20-11:59p	4.70	07/12-05:58p	07/16-07:30a
XB358G	XB358A	3-300-DV	4.00	07/02-06:00a 07/07-11:59p	2.50	07/02-09:12a	07/05-12:18p
XB358H	XB358A	ALL WELD W/MANHOLE	4.00	07/02-06:00a 07/08-11:59p	2.10	07/02-09:24a	07/06-10:08p
XB358K	XB358A	CAB PARTS-WC-SBLAST	4.00	07/02-06:00a 07/15-11:59p	2.80	07/09-09:23p	07/13-04:38a
XB358L	XB358A	300-500-WC-NR Q=1	4.00	07/02-06:00a 07/14-11:59p	5.10	07/07-10:12a	07/09-09:23p
XB358I	XB358L	300-500-WC QTY=1	4.00	07/02-06:00a 07/08-11:59p	2.60	07/02-10:12a	07/06-10:00a
XB358J	XB358L	WELD ON FF QTY=1	4.00	07/02-06:00a 07/08-11:59p	2.10	07/02-03:06p	07/06-10:00p

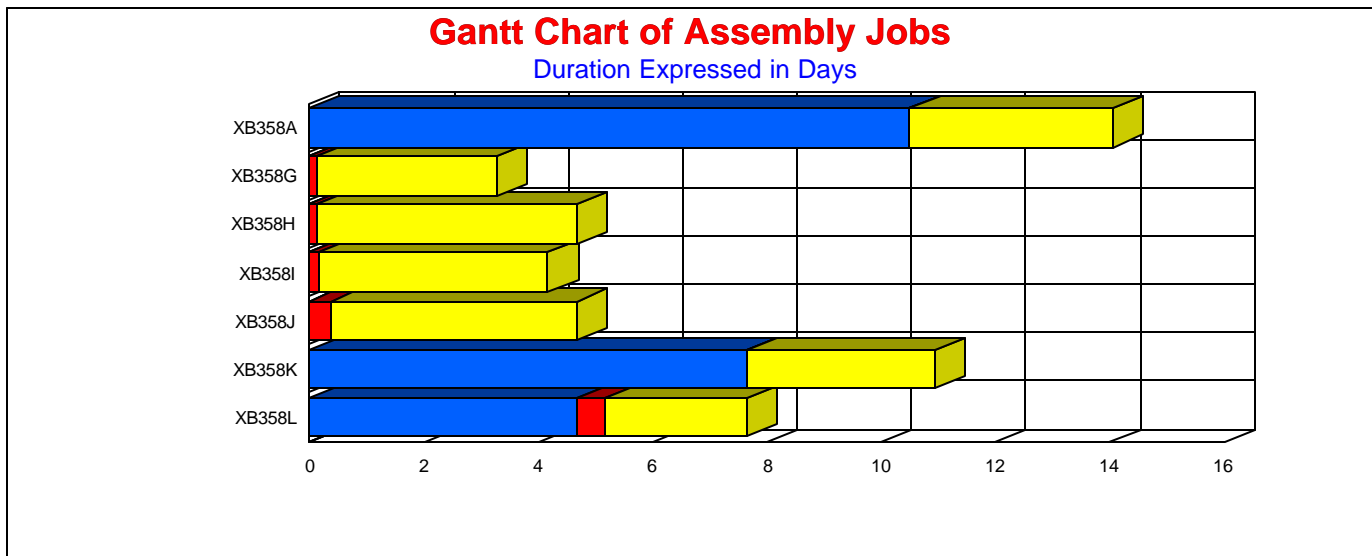



Assembly Job Gantt Chart

11/29/06

Order: XB360

Job ID	Assy Job	Job Description	Qty	Rel Date Due Date	Days Early <Late>	Estimated Start Date	Estimated Finish Date
XB360A		225-500-WC-<200 Q>1	4.00	07/02-06:00a 07/21-11:59p	1.70	07/13-04:52a	07/20-06:19a
XB360G	XB360A	3-300-DV	4.00	07/02-06:00a 07/08-11:59p	2.70	07/02-09:12a	07/06-07:54a
XB360H	XB360A	ALL WELD W/MANHOLE	4.00	07/02-06:00a 07/09-11:59p	2.30	07/02-05:24p	07/07-04:20p
XB360K	XB360A	CAB PARTS-WC-SBLAST	4.00	07/02-06:00a 07/15-11:59p	2.40	07/12-06:11p	07/13-03:02p
XB360L	XB360A	300-500-WC-1 RAD Q=1	4.00	07/02-06:00a 07/14-11:59p	2.20	07/07-02:42p	07/12-06:11p
XB360I	XB360L	300-500-WC QTY=1	4.00	07/02-06:00a 07/09-11:59p	2.50	07/02-06:12p	07/07-12:00p
XB360J	XB360L	WELD ON FF QTY=1	4.00	07/02-06:00a 07/09-11:59p	2.40	07/05-07:06a	07/07-02:42p

